ID	Nom de la tâche	Duration	Start	Finish
1	***FS02 - DIVERSITY FOR FREQUENT FAULTS***	***482 days***	***Thu 27/01/11***	***Fri 30/11/12***
2	**Meetings**	**208 days**	**Mon 12/12/11**	**Thu 27/09/12**
3	Meeting 1 -progress meeting on deliverables	0 days	Mon 12/12/11	Mon 12/12/11
4	Meeting 2 - progress meeting on deliverables	0 days	Thu 02/02/12	Thu 02/02/12
5	Meeting 3 -progress meeting on deliverables	0 days	Thu 08/03/12	Thu 08/03/12
6	Meeting 4 - progress meeting on deliverables	0 days	Wed 02/05/12	Wed 02/05/12
7	Meeting 5 - (if necessary) progress meeting on deliverables	0 days	Thu 28/06/12	Thu 28/06/12
8	Meeting 6 - (if necessary) convergence meeting	0 days	Thu 27/09/12	Thu 27/09/12
9	**FS02 - Actions 1,3,4 - CMF 23**	**386 days**	**Thu 27/01/11**	**Thu 19/07/12**
10	Submission of Stage 1 CMF	0 days	Thu 27/01/11	Thu 27/01/11
11	Submission of updated PCSR	0 days	Thu 31/03/11	Thu 31/03/11
12	Impact Analysis	50 days	Fri 22/04/11	Thu 30/06/11
13	Submission of Stage 2	0 days	Thu 30/06/11	Thu 30/06/11
14	ONR feedback - Meeting	0 days	Mon 12/12/11	Mon 12/12/11
15	**CMF 23**	**64 days**	**Mon 23/04/12**	**Thu 19/07/12**
16	CMF 23 - Handover package and draft Specification (Action from CC02-A1	29 days	Mon 23/04/12	Thu 31/05/12
17	Submission to ONR of draft handover package	0 days	Thu 31/05/12	Thu 31/05/12
18	ONR review and comments	15 days	Fri 01/06/12	Thu 21/06/12
19	Updated Specification / handover form	20 days	Fri 22/06/12	Thu 19/07/12
20	**FS02 - Action 2 - Increase in secondary steam flow**	**409 days**	**Thu 05/05/11**	**Tue 27/11/12**
21	Submission of Full response to TQ 1432	0 days	Thu 05/05/11	Thu 05/05/11
22	**Task 1 - Sensitivity study**	**223 days**	**Wed 21/09/11**	**Fri 27/07/12**
23	Study and report preparation	66 days	Wed 21/09/11	Wed 21/12/11
24	Submission of revised analysis	0 days	Wed 21/12/11	Wed 21/12/11
25	ONR Review	35 days	Thu 22/12/11	Wed 08/02/12
26	ONR feedback on deliverable - Meeting 2	0 days	Thu 02/02/12	Thu 02/02/12
27	**TQ 1593 - ONR comments on document**	**95 days**	**Mon 19/03/12**	**Fri 27/07/12**
28	TQ received	0 days	Mon 19/03/12	Mon 19/03/12
29	Part response to TQ 1593	16 days	Thu 22/03/12	Thu 12/04/12
30	Full response to TQ 1593	40 days	Mon 30/04/12	Fri 22/06/12
31	Submission of Full response to TQ 1593	0 days	Fri 22/06/12	Fri 22/06/12
32	ONR Review	25 days	Mon 25/06/12	Fri 27/07/12
33	**Task 2 - ALARP Analysis - CANCELLED**	**125 days**	**Mon 14/11/11**	**Fri 04/05/12**
40	**Task 3 - PCSR Update**	**77 days**	**Mon 13/08/12**	**Tue 27/11/12**
41	Draft PCSR chapter (chapter 16.5)	30 days	Mon 13/08/12	Fri 21/09/12
42	Transmission to ONR	0 days	Fri 21/09/12	Fri 21/09/12
43	ONR review	30 days	Mon 24/09/12	Fri 02/11/12
44	Update following ONR comments	17 days	Mon 05/11/12	Tue 27/11/12
45	Submission of final PCSR chapters	0 days	Tue 27/11/12	Tue 27/11/12
46	**FS02 - Actions 5 - Rod Drop**	**409 days**	**Thu 05/05/11**	**Tue 27/11/12**
47	Submission of Full response to TQ 1432	0 days	Thu 05/05/11	Thu 05/05/11
48	**Task 1 - Sensitivity study**	**198 days**	**Wed 21/09/11**	**Fri 22/06/12**
49	Complementary analysis and justification	66 days	Wed 21/09/11	Wed 21/12/11
50	Submission of revised analysis	0 days	Wed 21/12/11	Wed 21/12/11
51	ONR Review	35 days	Thu 22/12/11	Wed 08/02/12
52	ONR feedback on deliverable - Meeting 2	0 days	Thu 02/02/12	Thu 02/02/12
53	**TQ 1581 - ONR comments on document**	**79 days**	**Tue 06/03/12**	**Fri 22/06/12**
54	TQ received	0 days	Tue 06/03/12	Tue 06/03/12
55	Part response to TQ 1581	16 days	Fri 30/03/12	Fri 20/04/12
56	Full response to TQ 1581	20 days	Mon 30/04/12	Fri 25/05/12
57	Submission of Full response to TQ 1581	0 days	Fri 25/05/12	Fri 25/05/12
58	ONR Review	20 days	Mon 28/05/12	Fri 22/06/12
59	**Task 2 - documentation update - CANCELLED**	**108 days**	**Mon 28/05/12**	**Wed 24/10/12**
65	**Task 3 - PCSR Update**	**82 days**	**Mon 06/08/12**	**Tue 27/11/12**
66	Draft PCSR chapter (chapter 16.5)	35 days	Mon 06/08/12	Fri 21/09/12
67	Transmission to ONR	0 days	Fri 21/09/12	Fri 21/09/12
68	ONR review	30 days	Mon 24/09/12	Fri 02/11/12
69	Update following ONR comments	17 days	Mon 05/11/12	Tue 27/11/12
70	Submission of final PCSR chapters	0 days	Tue 27/11/12	Tue 27/11/12
71	**FS02 - Action 6 - Protection against loss of CVCS**	**419 days**	**Thu 17/02/11**	**Tue 25/09/12**
72	Submission of Full response to TQ 1432	0 days	Thu 17/02/11	Thu 17/02/11
73	**Task 1 - ALARP Analysis**	**220 days**	**Mon 23/05/11**	**Fri 23/03/12**
74	ALARP analysis of options and Report	45 days	Mon 23/05/11	Fri 22/07/11
75	Report - transmission to HSE	0 days	Fri 22/07/11	Fri 22/07/11
76	ONR review	40 days	Mon 24/10/11	Fri 16/12/11
77	ONR feedback on deliverable - Meeting 1	0 days	Mon 12/12/11	Mon 12/12/11
78	**TQ 1539 - ONR comments on document**	**72 days**	**Thu 15/12/11**	**Fri 23/03/12**
79	TQ received	0 days	Thu 15/12/11	Thu 15/12/11
80	Full response to TQ 1539	35 days	Mon 09/01/12	Fri 24/02/12
81	Submission of Full response	0 days	Fri 24/02/12	Fri 24/02/12
82	ONR Review	20 days	Mon 27/02/12	Fri 23/03/12
83	**Task 2 - PCSR update**	**74 days**	**Thu 14/06/12**	**Tue 25/09/12**
84	Draft PCSR chapter (chapter 14)	27 days	Thu 14/06/12	Fri 20/07/12
85	Transmission to ONR	0 days	Fri 20/07/12	Fri 20/07/12
86	ONR review	25 days	Mon 23/07/12	Fri 24/08/12
87	Update following ONR comments	22 days	Mon 27/08/12	Tue 25/09/12
88	Submission of final PCSR chapters	0 days	Tue 25/09/12	Tue 25/09/12
89	**FS02 - Action 7 - Homogeneous boron dilution with loss of TXS**	**433 days**	**Fri 01/04/11**	**Tue 27/11/12**
90	**Task 1 - ALARP analysis**	**365 days**	**Mon 13/06/11**	**Fri 02/11/12**
91	Analysis of options - ALARP conclusion	160 days	Mon 13/06/11	Fri 20/01/12
92	Report on ALARP conclusions	100 days	Mon 30/01/12	Fri 15/06/12
93	Meeting - Presentation of proposals	0 days	Thu 08/03/12	Thu 08/03/12
94	Transmission to ONR	0 days	Fri 15/06/12	Fri 15/06/12
95	ONR review	40 days	Mon 18/06/12	Fri 10/08/12
96	**TQ XXXX - ONR comments on document**	**60 days**	**Fri 10/08/12**	**Fri 02/11/12**
97	TQ received	0 days	Fri 10/08/12	Fri 10/08/12
98	Full response to TQ XXXX	40 days	Mon 13/08/12	Fri 05/10/12
99	Submission of Full Response	0 days	Fri 05/10/12	Fri 05/10/12
100	ONR Review	20 days	Mon 08/10/12	Fri 02/11/12

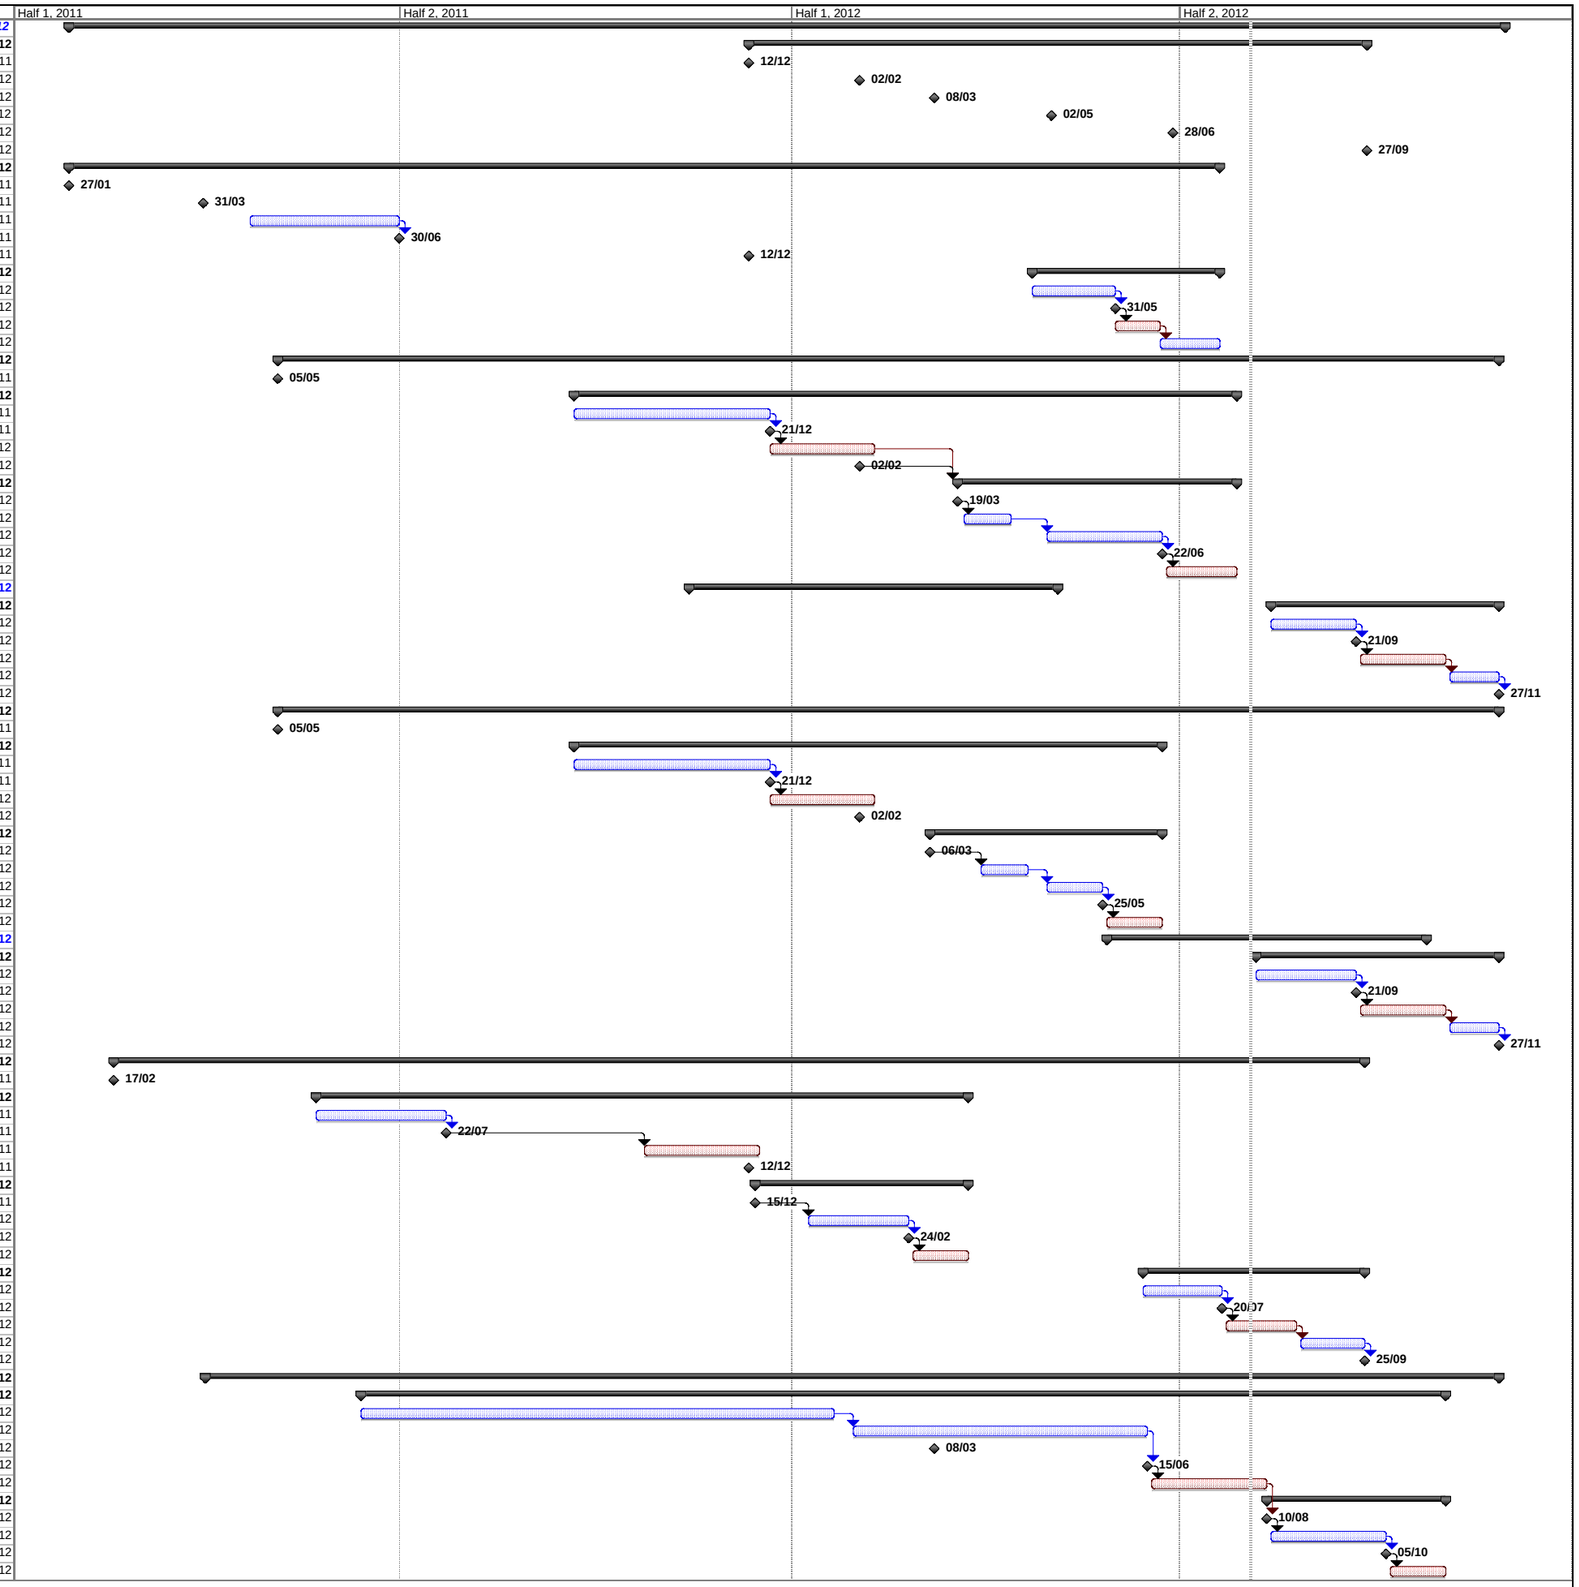

Tâche | Avancement | Récapitulative | Tâches externes | Échéance
Fractionnement | Jalon | Récapitulatif du projet | Jalons externes

ID	Nom de la tâche	Duration	Start	Finish
101	**Task 2 - documentation update**	**433 days**	**Fri 01/04/11**	**Tue 27/11/12**
102	**Update of document NEPR-F DC 580 -CANCELLED?**	**0 days**	**Fri 01/04/11**	**Fri 01/04/11**
104	Draft PCSR chapter (chapter 16.5)	50 days	Mon 16/07/12	Fri 21/09/12
105	Transmission to ONR	0 days	Fri 21/09/12	Fri 21/09/12
106	ONR review	30 days	Mon 24/09/12	Fri 02/11/12
107	Update following ONR comments	17 days	Mon 05/11/12	Tue 27/11/12
108	Submission of final PCSR chapters	0 days	Tue 27/11/12	Tue 27/11/12
109	**FS02 - Action 8 - Diversity for support systems frequent faults**	**436 days**	**Fri 01/04/11**	**Fri 30/11/12**
110	**Task 1 - ALARP Analysis SBO**	**140 days**	**Mon 27/02/12**	**Fri 07/09/12**
111	ALARP analysis for SBO Start-up	70 days	Mon 27/02/12	Fri 01/06/12
112	Transmission to ONR	0 days	Fri 01/06/12	Fri 01/06/12
113	ONR review	30 days	Mon 04/06/12	Fri 13/07/12
114	Update following ONR comments	40 days	Mon 16/07/12	Fri 07/09/12
115	Submission of final document	0 days	Fri 07/09/12	Fri 07/09/12
116	**Task 2 - Diversity analysis for frequent faults**	**170 days**	**Mon 09/04/12**	**Fri 30/11/12**
117	Diversity analysis for frequent faults identified in FS05	60 days	Mon 09/04/12	Fri 29/06/12
118	Transmission to ONR	0 days	Fri 29/06/12	Fri 29/06/12
119	ONR review	25 days	Mon 02/07/12	Fri 03/08/12
120	Update following ONR comments	40 days	Mon 06/08/12	Fri 28/09/12
121	Submission of final document	0 days	Fri 28/09/12	Fri 28/09/12
122	**TQ XXXX - ONR comments on document**	**45 days**	**Fri 28/09/12**	**Fri 30/11/12**
127	**Task 2 - Documentation update -**	**433 days**	**Fri 01/04/11**	**Tue 27/11/12**
128	**Update of document NEPR-F DC 580 - CANCELLED**	**391 days**	**Fri 01/04/11**	**Fri 28/09/12**
131	Draft PCSR chapter	45 days	Mon 23/07/12	Fri 21/09/12
132	Transmission to ONR	0 days	Fri 21/09/12	Fri 21/09/12
133	ONR review	30 days	Mon 24/09/12	Fri 02/11/12
134	Final PCSR chapter	17 days	Mon 05/11/12	Tue 27/11/12
135	Submission of final documentation	0 days	Tue 27/11/12	Tue 27/11/12
136	**FS02 - Action 9 - Diversity for safe state**	**397 days**	**Mon 23/05/11**	**Tue 27/11/12**
137	**Task 1 - Analysis for identified frequent faults**	**290 days**	**Mon 23/05/11**	**Fri 29/06/12**
138	Analysis of diversity for safe shutdown state and update of NEPR-F DC 58(	45 days	Mon 23/05/11	Fri 22/07/11
139	Transmission to ONR	0 days	Fri 22/07/11	Fri 22/07/11
140	ONR review	35 days	Mon 31/10/11	Fri 16/12/11
141	ONR feedback on deliverable - Meeting 1	0 days	Mon 12/12/11	Mon 12/12/11
142	**TQ 1579 - ONR comments on document**	**75 days**	**Mon 05/03/12**	**Fri 15/06/12**
143	TQ received	0 days	Mon 05/03/12	Mon 05/03/12
144	Full response to TQ 1579	40 days	Mon 26/03/12	Fri 18/05/12
145	ONR Review	20 days	Mon 21/05/12	Fri 15/06/12
146	**TQ 1595 - ONR comments on document**	**66 days**	**Fri 30/03/12**	**Fri 29/06/12**
147	TQ received	0 days	Fri 30/03/12	Fri 30/03/12
148	Acknowledgment to TQ 1595	20 days	Fri 30/03/12	Thu 26/04/12
149	Full response to TQ 1595	30 days	Mon 23/04/12	Fri 01/06/12
150	ONR Review	20 days	Mon 04/06/12	Fri 29/06/12
151	**Task 2 - Analysis for identified frequent faults following FS05 - DATE TBC**	**115 days**	**Mon 23/04/12**	**Fri 28/09/12**
152	Analysis of diversity for safe shutdown state and update of NEPR-F DC 58(	50 days	Mon 23/04/12	Fri 29/06/12
153	Submission of revised analysis	0 days	Fri 29/06/12	Fri 29/06/12
154	ONR review	30 days	Mon 02/07/12	Fri 10/08/12
155	Update following ONR comments	35 days	Mon 13/08/12	Fri 28/09/12
156	Submission of final documentation	0 days	Fri 28/09/12	Fri 28/09/12
157	**Task 3 - Documentation update**	**87 days**	**Mon 30/07/12**	**Tue 27/11/12**
158	Draft PCSR chapter (16.5 and 14.7)	40 days	Mon 30/07/12	Fri 21/09/12
159	Transmission to ONR	0 days	Fri 21/09/12	Fri 21/09/12
160	ONR review	30 days	Mon 24/09/12	Fri 02/11/12
161	Update following ONR comments	17 days	Mon 05/11/12	Tue 27/11/12
162	Submission of final documentation	0 days	Tue 27/11/12	Tue 27/11/12

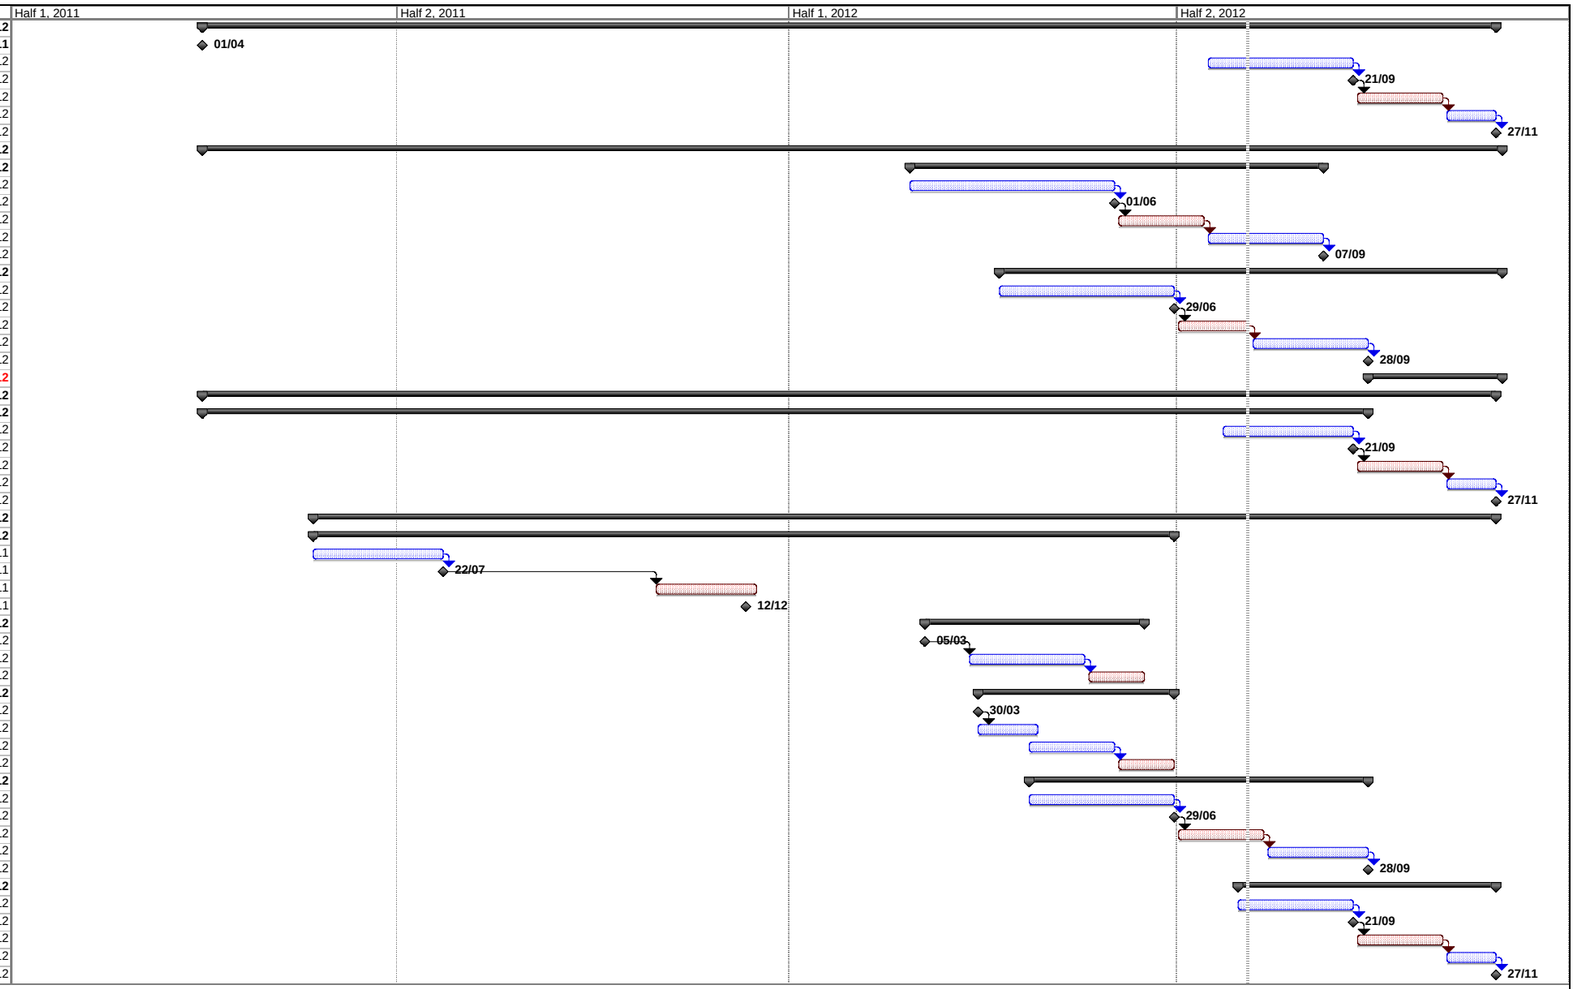

Tâche | Avancement | Récapitulative | Tâches externes | Échéance
Fractionnement | Jalon | Récapitulatif du projet | Jalons externes
